MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8

Construction of R.C.C. drain opp to Anjaneya temple Abbigere Village in ward no-12

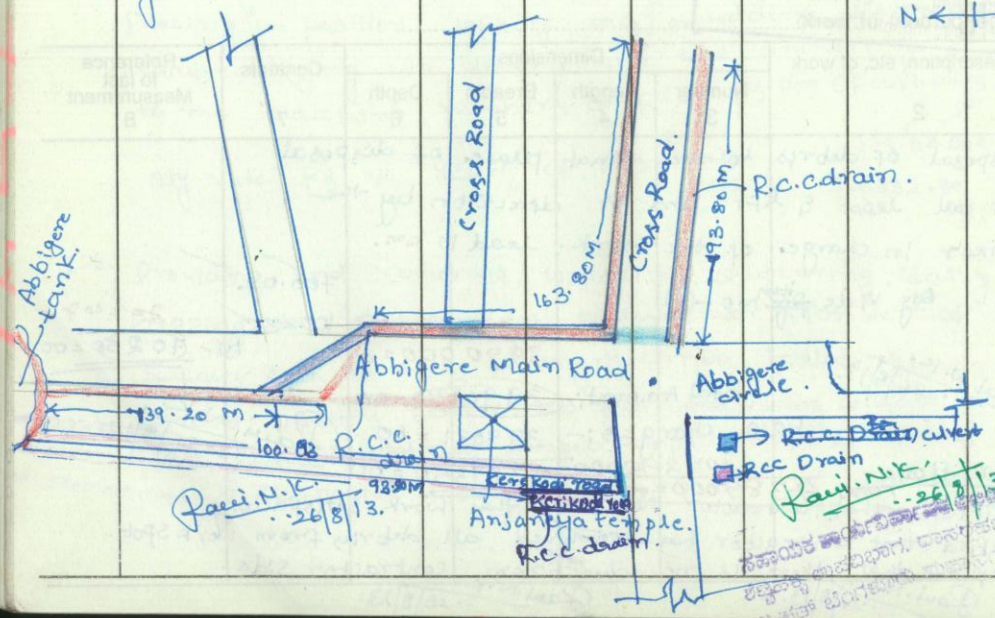

AEE[S]SD[S]B[1]91/13-14

BR 293/30.8.13

29-8-13

M.A.R. 57 (Rule 116)

Measurement Book

No. C/09 165653

Serial No. 1st & Final.

Name of work Construction of R.C.C. drain opp Anjaneya temple Abbigere Village Shettyhalli Sub-Division. From ..... To .....

Name of Contractor or nature of Agency Technical Manager (West) KRIDL

Date of commencement of work NO.PE|DD|HO|240|12-13 D:1-28|11|2012 JCi- 0/2-012-0000109 Est cost:-40.0 lakhs.

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Measured on 29/8/13						
I-1	Dismantaling Size stone masonry in clay mortar / lime mortar / cement mortar and stacking the Size stone within a radius of 50m and removing the debris to a distance upto 200m complete as per Specification.						
	Dly vide Pg No 165653/1 of this M.B.					62.64 cum @ 130.68	
						Rs:- 8186.00	
I-2	Earth work excavation for foundation of buildings culverts water Supply, Sanitary lines and electrical conduits either in Pits or in trenches 1.5m and above in Width in ordinary Soil not exceeding 1.5m in depth including dressing the bottom and sides of Pits after breaking of clods complete as per specification						

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
I-5.	Providing TMT steel reinforcement for R.C.C. work including straightening cutting, bending hooking placing in position lapping and/or welding wherever required tying with binding wire and anchoring to the adjoining members complete as per specifications						
	Qty vide pg No 165660/1 of this M.B.					175.34 Mt. @ 6382=80 Rs - 1122352=00	
I-6.	Providing and removing, centering, shuttering, Strutting Propping etc., and removal of form work for vertical Surfaces such as walls at any thickness including attached pilasters, buttresses plinth and string courses cost of all materials labour complete as per specifications						
	Qty vide pg No 165660/2 of this M.B.					1749.60 Sqm @ 555=12 Rs - 971238=00	

Audited and admitted Rs 4389000=00
Passed by Cheque for Rs 3822350=00
(3822351=00)
Serial No. 568649=00
566649=00
by Sub Divisional Officer
Name of work
Name of Contractor of nature of Agency
Date of commencement of work
Executive Engineer
Accounts Superintendent
R.B. Nellore

M.A.R. 57 (Rule 116)

Measurement Book No. C/09 165656

From To

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
I-7	Disposal of debris to the final place of disposal with all lead & lift and as direction by the engineer in charge of the work. lead to km.					700.02	
	Qty vide ~~pitn~~ No - (1)					@ 100=35 Rs - 70247 - 70250=00	
	Deduct Dismantling Amount (-) 2000=00 towards VSM. Rs.				3990000=0		
	Total Amount; -				3990319=00		
	KRIDL charges;-				399031=00		
	1 Certificate 10% 399000=				4389350=00		
	1) Certified that contractor has done the work satisfactory.						
	2) certified that contractor has removed all debris from work spot.						
	3) certified that there is no due from contractor side.						

Rani.N.K. 26/8/13.
Rani.N.K. 26/8/13.
Rani.N.K. 26/8/13.

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	V	2	48.20	0.15	1.20	17.35 cum	
	B	1	48.20	1.10	0.15	7.95 cum	
	V	2	39.40	0.15	1.20	14.18 cum	
	B	1	39.40	1.10	0.15	6.50 cum	
	V	2	50.0	0.15	1.20	18.0 cum	
	B	1	50.0	1.10	0.15	8.25 cum	
	V	2	1.60	0.15	1.20	8.45 cum	
	B	1	1.60	1.10	0.15	1.58 cum	
	V	2	50.0	0.15	0.90	13.50 cum	
	B	1	50.0	1.10	0.15	8.25 cum	
	V	2	50.0	0.15	0.90	13.50 cum	
	B	1	50.0	1.10	0.15	8.25 cum	

CEPC
Kevekadi Road
26/6/13
ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು ಕರ್ನಾಟಕ ಕಾಲ್ಯಾಣ ಕರ್ನಾಟಕ ಪ್ರದೇಶಾಭಿವೃದ್ಧಿ ಮಂಡಳಿಯ ಕೇಂದ್ರಸ್ಥಾನ ಲಘುಪಾಲಾಗ. ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರ ಕಛೇರಿ ಜಲಮಂಡಳಿ ಬಿಲ್ಡಿಂಗ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

CEPC
2918
EE(D)

M.A.R. 57 (Rule 116)

Measurement Book No. C/09 165655

Serial No.....

Name of work.....From.....To.....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
		2	43.80	0.15	0.90	11.82 cum	
		1	43.80	1.10	0.15	7.22 cum	
	Covering Precast Slabs.	1	504.80	0.90	0.10	45.43 cum	
	Total Length	2	7.0	0.75+0.60 / 2	1.0	9.45 cum	
	43.20+48.60+26.20+45.80	2	10.0	0.75+0.60 / 2	0.90	12.15 cum	
	+48.20+39.40+59.6+50.0	1	7.0	1.10	0.23	1.77 cum	
	+50.0+50.0+43.80=504.80	1	10.0	1.10	0.23	2.53 cum	
						311.34 cum	304.44
						283.84 cum	1432.650
						5047=92 Rs.	1432802.00

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು ಕರ್ನಾಟಕ ಕಾಲ್ಯಾಣ ಕರ್ನಾಟಕ ಪ್ರದೇಶಾಭಿವೃದ್ಧಿ ಮಂಡಳಿಯ ಕೇಂದ್ರಸ್ಥಾನ ಲಘುಪಾಲಾಗ. ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರ ಕಛೇರಿ ಜಲಮಂಡಳಿ ಬಿಲ್ಡಿಂಗ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

Limited to tender @

CEPC
2918
EE(D)
